



September 16, 2022

Dear Sir or Madam:

Re: Blackwater Gold Project Schedule of Activities: Environmental Assessment Decision Statement Conditions 6.6 and 6.7

In accordance with Decision Statement (DS) schedule conditions 11.3 and 11.4, BW Gold Ltd. (BW Gold) is required to provide an updated schedule outlining all activities required to carry out the Blackwater Project by September 30 each year, and to provide an update upon revision of the schedule. To conform to the DS conditions, these schedules are to be provided to:

- The Impact Assessment Agency of Canada (DS conditions 11.3 and 11.4)
- Indigenous holders of provincially registered traplines, whose traplines overlap with the Designated Project area (DS Condition 6.6).
- Tenure holders, including trappers, guide outfitters and range tenure holders whose activities overlap with the Designated Project area (DS Condition 6.7).

For your reference, the Decision Statement Conditions can be found at <https://iaac-aeic.gc.ca/050/documents/p80017/129205E.pdf>.

The Blackwater Mine has launched a community feedback mechanism. Feedback is used to improve how we operate and strengthen our relationships with Indigenous nations, communities, individuals, and organizations. Individuals wishing to provide feedback have the option to share open or anonymous comments which will be addressed in a timely, transparent, and respectful manner. All feedback submissions will be acknowledged within two days or less and we have a commitment to resolve and report back to complaints within 30 days or less. More information on the feedback mechanism is posted on our website at www.artemisgoldinc.com.

For additional updates related to project status, current version of plans and other documentation please visit the BW Gold website (<https://blackwatergoldmine.com/>) and sign up for BW Gold notifications to be made aware of new website content or updates to project materials such as schedules and work plans.

Yours truly,

<Original signed by>

Ryan Todd
VP Environment and Social Responsibility
Artemis Gold Inc.

Attachment: Project Schedule



Attachment
Decision Statement Schedule 11 (September 19, 2022)

Blackwater Gold Project

0 - Phase Roll Up

Activity ID	Activity Name	Original Duration	Start	Finish	Year																							
					2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040	2041			
Blackwater Gold Project		48.2y	01-Jul-2022	09-Jan-2070	▼																							
1 - Major Milestones		48.2y	01-Jul-2022	09-Jan-2070	▼																							
2 - Early Works		0.7y	01-Jul-2022	03-Mar-2023	▼																							
3 - Major Works (Construction)		1.6y	10-Feb-2023	31-Aug-2024	▼																							
4 - Year +1 to Year +5		5.0y	07-Sep-2024	12-Aug-2029	▼																							
5 - Year +6 to Year +10		5.0y	12-Aug-2029	17-Jul-2034	▼																							
6 - Year +11 to Year +18		11.0y	17-Jul-2034	20-May-2045	▼																							
7 - Year +19 to Year +23		5.0y	05-Jun-2042	10-May-2047	▼																							
8 - Year +24 to Year +45		22.0y	10-May-2047	14-Jan-2069	▼																							
9 - Post Closure Year +46		1.0y	14-Jan-2069	09-Jan-2070	▼																							


- Critical Remaining Work
- Remaining Work
- summary

TASK filter: All Activities

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project

0 - Phase Roll Up

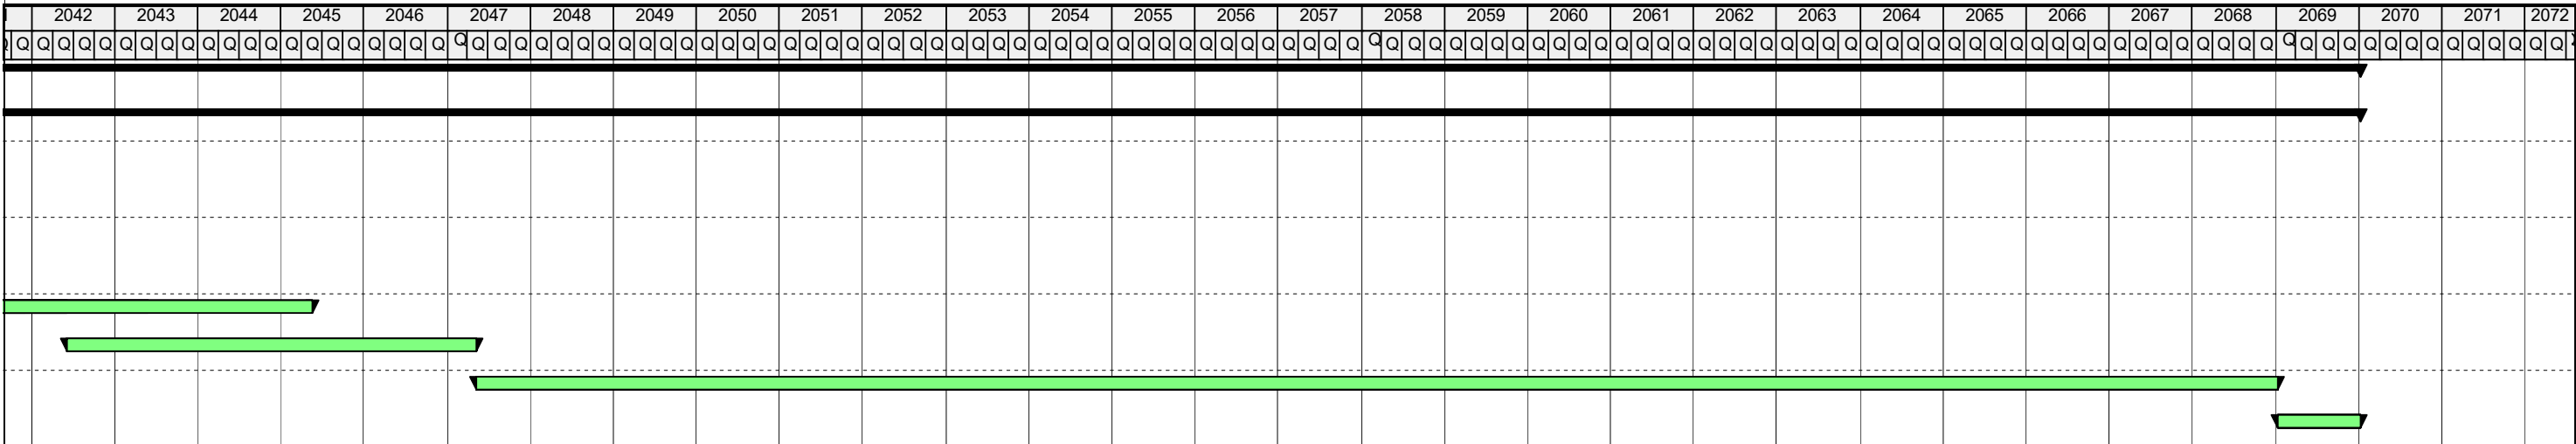

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: All Activities

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project


1 - Milestones

Activity ID	Activity Name	Original Duration	Start	Finish	2020	2021	2022	2023	2024	2025	2026	2027	2028	2029	2030	2031	2032	2033	2034	2035	2036	2037	2038	2039	2040			
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
Blackwater Gold Project		48.2y	01-Jul-2022	09-Jan-2070																								
1 - Major Milestones		48.2y	01-Jul-2022	09-Jan-2070																								
A3900	Start of Early Works	0.0y	01-Jul-2022*		01-Jul-2022*	◆																						
A3910	End of Early Works	0.0y		03-Mar-2023			◆ 03-Mar-2023																					
A3920	Start of Major Works	0.0y	10-Feb-2023*		10-Feb-2023*	◆																						
A3930	End of Major Works	0.0y		31-Aug-2024				◆ 31-Aug-2024																				
A3940	Process Facility First Gold Pour	0.0y	07-Sep-2024					◆ 07-Sep-2024																				
A3950	Start Year +1	0.0y	07-Sep-2024					◆ 07-Sep-2024																				
A3960	End Year +5	0.0y		12-Aug-2029											◆ 12-Aug-2029													
A3970	Start Year +6	0.0y	12-Aug-2029												◆ 12-Aug-2029													
A3980	End Year +10	0.0y		17-Jul-2034																								
A3990	Start Year +11	0.0y	17-Jul-2034																									
A4000	End Year +18	0.0y		20-May-2045																								
A4010	Start Year +19	0.0y	05-Jun-2042																									
A4020	End Year +23	0.0y		10-May-2047																								
A4030	Start Year +24	0.0y	10-May-2047																									
A4040	End Year +45	0.0y		14-Jan-2069																								
A4050	Start Year +46 Post Closure	0.0y	14-Jan-2069																									
A4060	End Year +46 Post Closure	0.0y		09-Jan-2070																								

<p> Critical Remaining Work summary Remaining Work ◆ Milestone </p>	<p>TASK filter: WBS .</p>	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="text-align: center;">Date</th> <th style="text-align: center;">Revision</th> </tr> <tr> <td>15-Sep-2022</td> <td>V.2: Prepared pursuant to:</td> </tr> <tr> <td></td> <td style="text-align: center;">Blackwater Decision Statement condition 11.2</td> </tr> </table>	Date	Revision	15-Sep-2022	V.2: Prepared pursuant to:		Blackwater Decision Statement condition 11.2	<table border="1" style="width: 100%; border-collapse: collapse;"> <tr> <th style="text-align: center;">Checked</th> <th style="text-align: center;">Approved</th> </tr> <tr> <td style="text-align: center;">BW</td> <td style="text-align: center;">SEB / RT</td> </tr> </table>	Checked	Approved	BW	SEB / RT
Date	Revision												
15-Sep-2022	V.2: Prepared pursuant to:												
	Blackwater Decision Statement condition 11.2												
Checked	Approved												
BW	SEB / RT												

Blackwater Gold Project

1 - Milestones

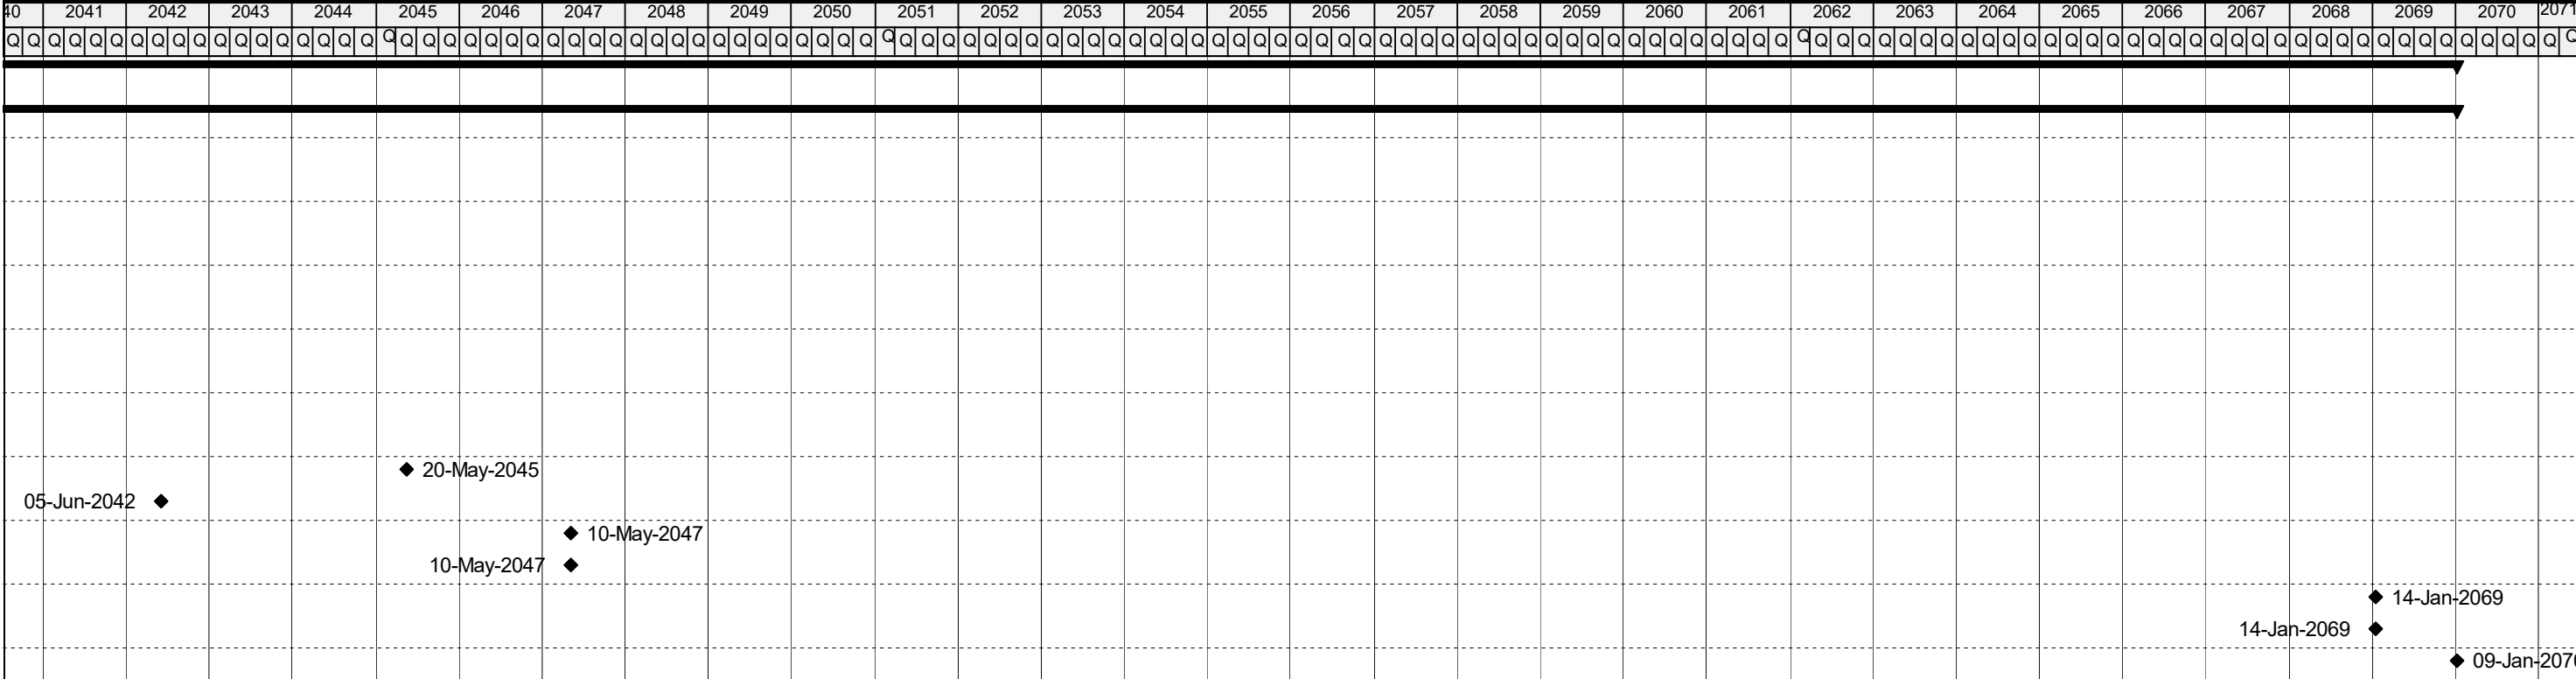

05-Jun-2042 ◆

20-May-2045 ◆

10-May-2047 ◆

14-Jan-2069 ◆

14-Jan-2069 ◆

09-Jan-2070 ◆

<p>█ Critical Remaining Work</p> <p>█ Remaining Work</p> <p>◆ Milestone</p>	<p>▼ summary</p>	<p>TASK filter: WBS .</p>	Date	Revision	Checked	Approved
			15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project 2 - Early Works

Activity ID	Activity Name	Original Duration	Start	Finish	2022						2023					
					Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	
Blackwater Gold Project		0.7y	01-Jul-2022	03-Mar-2023												
2 - Early Works		0.7y	01-Jul-2022	03-Mar-2023												
Plant Site		0.5y	17-Sep-2022	03-Mar-2023												
A1010	Vegetation clearing, grubbing and site leveling	0.5y	17-Sep-2022	03-Mar-2023												
Construction Camp 245 Persons		0.5y	01-Jul-2022	19-Dec-2022												
A1020	Clear Core	0.2y	01-Jul-2022	13-Sep-2022												
A1030	Earthworks	0.1y	13-Sep-2022	08-Oct-2022												
A1040	Place Dorms	0.1y	08-Oct-2022	17-Nov-2022												
A1050	Snow Roofs	0.1y	30-Oct-2022	07-Dec-2022												
A1060	Finishing Works (Elec/Plumb)	0.1y	03-Nov-2022	19-Dec-2022												

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project

3 - Major Works

Activity ID	Activity Name	Original Duration	Start	Finish	2023												2024																
					Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov				
Blackwater Gold Project																																	
3 - Major Works (Construction)																																	
Open Pit																																	
A1120	Vegetation clearing, grubbing and surface preparation of initial pit phases	0.6y	10-Feb-2023	30-Sep-2023	10-Feb-2023																												
A1140	Commissioning of initial mine fleet (Year -2) and addition to in-pit mine fleet (Year -1)	0.8y	09-Aug-2023	04-Jun-2024																													
A1150	Starter Pit – Mining to 1,610 metres above sea level (masl) bench (Year -2)	0.6y	06-Jan-2024	24-Jul-2024																													
A1160	Construction Borrow Pit – Mining to 1,510 masl bench (Year -2)	0.6y	13-Feb-2024	31-Aug-2024																													
Process Plant																																	
A1170	Foundation construction and initial stockpiling at ROM (Year -2, Year -1)	1.6y	10-Feb-2023	31-Aug-2024	10-Feb-2023																												
A1180	Construction of facilities to pre-commissioning (Year -1)	1.2y	10-Jun-2023	31-Aug-2024																													
Tailings Storage Facility (TSF)																																	
A1190	Additional vegetation clearing of TSF	0.7y	10-Feb-2023	22-Oct-2023	10-Feb-2023																												
A1200	Construction of the diversion works including the Davidson Creek Diversion System and Mine Area Creek Diversion	0.2y	12-Mar-2023	11-May-2023	12-Mar-2023																												
A1210	SCP and the associated inlet channels	0.6y	27-Feb-2023	06-Oct-2023	27-Feb-2023																												
A1220	Main Dam C – Excavation of cut-off-trench (COT) and initial fill placement (Year -2)	1.0y	16-Sep-2023	31-Aug-2024																													
A1230	Main Dam C Stage 1 construction to 1,273 masl (Year -1)	0.5y	26-Feb-2024	31-Aug-2024																													
A1240	TSF C Pond – Starter pond initiation at the Diversion Berm (Year -2); Receipt of water from drainage area	0.3y	20-May-2024	31-Aug-2024																													
A1250	Disposal of PAG and ML waste rock in designated disposal area located between the Diversion Berm and Main Dam C	0.1y	19-Jul-2024	31-Aug-2024																													
A1260	Water reclaim pipeline and reclaim pump systems from TSF C Pond – Siting and construction to pre-commissioning	0.5y	04-Mar-2024	31-Aug-2024																													
A1270	Tailings distribution pipeline constructed -processing facility to the west side TSF C – Siting and const. to pre-comm	0.5y	04-Mar-2024	31-Aug-2024																													
A1280	Construction of the IECD, pond and pumpback system (Year -1)	0.4y	03-Apr-2024	31-Aug-2024																													
Waste Stockpiles (WSF)																																	
A1290	Vegetation clearing, grubbing, and surface preparation as required	0.2y	15-Aug-2023	14-Oct-2023																													
A1300	Construction of Lower WSF water mgmt systems, including water collection channels & the Lower WSF Collection Pond	0.5y	04-Mar-2024	31-Aug-2024																													
A1310	Lower Waste Stockpile – Development of lift to 1,420 masl (Year -1)	0.5y	04-Mar-2024	31-Aug-2024																													
Low Grade Ore (LGO) Stockpile																																	
A1320	Vegetation clearing, grubbing, and surface preparation as required	0.5y	07-Aug-2023	26-Jan-2024																													
A1330	Construction of water mgmt systems, including non-contact water diversions, contact water collection channels	0.4y	26-Jan-2024	14-Jun-2024																													
A1340	Construction of water mgmt systems LGO Collection Pond, stockpile sub-grade preparation, and associated liner systems	0.5y	14-Mar-2024	31-Aug-2024																													
A1350	Stockpiling of LGO Stockpile (lower grade ore) to 1,440 masl (Year -1)	0.4y	24-Mar-2024	31-Aug-2024																													

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project

3 - Major Works

































Activity ID	Activity Name	Original Duration	Start	Finish	2023												2024															
					Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov			
A1590	Operations camp – Construction, commissioning, and operation (Year -2)	0.7y	10-Feb-2023	23-Oct-2023	10-Feb-2023													23-Oct-2023														
A1600	Exploration camp – Operation (Year -2); relocation of facilities to operations camp pad (Year -1)	0.5y	25-Jul-2023	21-Jan-2024						25-Jul-2023								21-Jan-2024														
A1610	Truck shop and wash/Mine office – Construction, commissioning, and operation (Year -1)	1.4y	12-Mar-2023	19-Jul-2024			12-Mar-2023																				19-Jul-2024					
A1620	Ready Line and Bulk Fuel Storage area – Construction, commissioning, and operation (Year -1)	1.2y	11-Apr-2023	04-Jun-2024				11-Apr-2023															04-Jun-2024									
A1630	Waste management facilities – Construction, commissioning, and operation (Year -1)	0.7y	22-Nov-2023	19-Jul-2024											22-Nov-2023									19-Jul-2024								
A1640	Potable and fire water supplies – Construction, commissioning, and operation (Year -1)	1.0y	25-Jul-2023	19-Jul-2024						25-Jul-2023															19-Jul-2024							
A1650	Helipad – Construction, commissioning, and operation (Year -1)	0.5y	21-Jan-2024	19-Jul-2024													21-Jan-2024									19-Jul-2024						
Borrow Pits, Aggregate Screening and Concrete Batch Plant		1.3y	10-Feb-2023	03-Jun-2024																												
A1660	Borrow, aggregate screening and concrete batch plant area – Construction and operation (Year -2)	0.7y	10-Feb-2023	09-Oct-2023	10-Feb-2023													09-Oct-2023														
A1670	Borrow, aggregate screening and construction laydown area – Construction and operation (Year -2)	0.8y	10-Feb-2023	08-Dec-2023	10-Feb-2023													08-Dec-2023														
A1680	TSF and FWR embankment borrow areas (Year -1)	0.8y	30-Aug-2023	03-Jun-2024						30-Aug-2023															03-Jun-2024							
Offsite Infrastructure		1.3y	10-Feb-2023	05-May-2024																												
A1710	Construction of transmission line from Glenannan substation to mine site	1.3y	10-Feb-2023	05-May-2024	10-Feb-2023																				05-May-2024							
A4090	Decommissioning of the Mount Davidson Exploration Road	0.3y	05-Feb-2024	05-May-2024													05-Feb-2024					05-May-2024										

Critical Remaining Work
 Remaining Work
 summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project 4 - Year +1 to Year +5

Activity ID	Activity Name	Original Duration	Start	Finish	2024		2025				2026				2027				2028				2029				2030	
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
Blackwater Gold Project																												
4 - Year +1 to Year +5																												
Open Pit																												
A1730	Continued clearing of pit area	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1740	Extraction Method - Diesel drill, blast and shovel; Addition of electric drill and shovel (Year +5)	1.0y	17-Aug-2028	12-Aug-2029																								
A1750	Installation of 4.16 kV substation to power electric drill and shovel (Year +5)	1.0y	17-Aug-2028	12-Aug-2029																								
A1760	Staged increase to in-pit mine fleet (Year +1)	1.0y	07-Sep-2024	02-Sep-2025	07-Sep-2024																							
A1762	Staged increase to in-pit mine fleet (Year +4)	1.0y	23-Aug-2027	17-Aug-2028																								
A1764	Staged increase to in-pit mine fleet (Year +5)	1.0y	17-Aug-2028	12-Aug-2029																								
A1770	Construction Borrow Pit – Mining to pit bottom 1,450 masl (Year +2)	1.0y	02-Sep-2025	28-Aug-2026																								
A1780	Starter Pit – Mining to pit bottom 1,450 masl (Year +3)	1.0y	28-Aug-2026	23-Aug-2027																								
A1790	East Pushback 1 – Mining to pit bottom 1,460 masl (Year +4)	1.0y	23-Aug-2027	17-Aug-2028																								
A1800	East Pushback 2 – Mining to 1,460 masl bench (Year +5)	1.0y	17-Aug-2028	12-Aug-2029																								
A1810	West Pushback – Mining to 1,540 masl bench (Year +5)	1.0y	17-Aug-2028	12-Aug-2029																								
Process Facilities																												
A1820	Phase 1 commissioning and operations to 4.5 Mt per annum (Year +1) and 5.5 Mt per annum (Year +2)	2.0y	07-Sep-2024	28-Aug-2026	07-Sep-2024																							
A1830	Conduct upgrades to increase throughput to 12 Mt per annum (Year +5)	3.0y	28-Aug-2026	12-Aug-2029																								
Tailings Storage Facility (TSF)																												
A1840	Main Dam C – Monitoring and annual raises up to 1,312 masl (Year +5)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1850	TSF C Pond – Receipt of discharge from mine site drainage network, IECD pond, and final ECD pond	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1860	Additional receipt of discharge from water accumulated behind Main Dam D initial fill areas;	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1870	With Impoundment of PAG and ML waste rock and tailings Serves as process water source	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1880	Main Dam D – Initial construction of Stage 1 to 1,256 masl (Year +5)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1890	Water reclaim pump systems in the TSF C Pond used to reclaim water to the mill to support ore processing	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1900	Expansion of water reclaim systems coinciding with processing facility expansions - Siting, Const & comm (Year +5)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1910	PAG/NAG3 waste rock disposal occurs within TSF C adjacent to Main Dam C	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1920	Tailing distribution systems and pipeline convey tailings to discharge location at west side of TSF C	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1930	IECD and pond – Operational with pumpback to the TSF C Pond	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
Waste Stockpiles (WSF)																												
A1940	Vegetation clearing, grubbing, and surface preparation as required	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
A1950	Lower Waste Stockpile – Stockpiling to 1,450 masl (Year +5)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024																							
Low Grade Ore (LGO) Stockpiles																												

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: Year 1 to 5.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project 4 - Year +1 to Year +5

Activity ID	Activity Name	Original Duration	Start	Finish	Timeline (2024-2030)																											
					Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	
A1960	Vegetation clearing, grubbing, and surface preparation as required	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A1970	Stockpiling of LGO Stockpile (lower grade ore) to lift height 1,500 masl (Year +3)	1.0y	28-Aug-2026	23-Aug-2027	28-Aug-2026 23-Aug-2027																											
A1980	Stockpiling of LGO Stockpile Pile A (higher grade ore) to lift height 1,470 masl (Year +3)	1.0y	28-Aug-2026	23-Aug-2027	28-Aug-2026 23-Aug-2027																											
Water Management Structures		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A1990	Open Pit dewatering	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2000	WMP outflows pumped to Processing Plant and FWR	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
Water Treatment		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2010	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharging to the TSF C Pond along with tailing	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2020	Treatment of waters accumulating in the Open Pit and runoff from the Lower Waste Stockpile treated by Metals WTP	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2030	Treated water is used at the mill and excess treated water conveyed to WMP	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2040	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
Mine Service and Haul Roads		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2050	Ex-pit haul roads – Expansion to service development of the pit	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2060	In-pit haul roads – Expansion to service development of the pit	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
Mine Access Road (MAR)		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A1110	Tree clearing, bulk excavation and grading, surfacing and installation of bridges	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
Ready Line and Bulk Fuel Supply		1.0y	23-Aug-2027	17-Aug-2028	23-Aug-2027 17-Aug-2028																											
A2070	Fuel storage expanded to 300,000 L (Year +4)	1.0y	23-Aug-2027	17-Aug-2028	23-Aug-2027 17-Aug-2028																											
Ongoing Use and Maintenance		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2080	Topsoil stockpiles	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2090	Central Diversion System, WMP, and FWR	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2100	Surface drainage for infrastructure	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2110	Mine service roads	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2120	Power supply and distribution	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2130	Explosives storage facility	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2140	Ancillary facilities	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2150	Borrow pits and aggregate and concrete batch plants (Plant expansion)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
Off-Site Infrastructure		5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A1690	Decommissioning of Exploration Access Road	1.0y	18-Jun-2028	13-Jun-2029	18-Jun-2028 13-Jun-2029																											
A2160	Transmission line	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A2170	Airstrip and airstrip access road – Construction and connection to Mine Access Road (MAR)	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											
A4120	Installation of Freshwater Supply System and Pumping and Pipeline systems from Tatelkuz Lake	5.0y	07-Sep-2024	12-Aug-2029	07-Sep-2024 12-Aug-2029																											

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: Year 1 to 5.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project 5 - Year +6 to Year +10


























Activity ID	Activity Name	Original Duration	Start	Finish	2029				2030				2031				2032				2033				2034				2035			
					Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2
A2600	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP	5.0y	12-Aug-2029	17-Jul-2034																												
Ongoing Use and Maintenance		5.0y	12-Aug-2029	17-Jul-2034																												
A2610	Topsoil stockpiles erosion control and invasive plant management	5.0y	12-Aug-2029	17-Jul-2034																												
A2620	Central and Northern Diversion systems and Central Water Transfer Pond North and South Interception trenches	5.0y	12-Aug-2029	17-Jul-2034																												
A2630	Pit dewatering	5.0y	12-Aug-2029	17-Jul-2034																												
A2640	Fresh Water Reservoir (FWR)	5.0y	12-Aug-2029	17-Jul-2034																												
A2650	Surface drainage for Infrastructure	5.0y	12-Aug-2029	17-Jul-2034																												
A2660	Mine service roads	5.0y	12-Aug-2029	17-Jul-2034																												
A2670	Ex-pit haul roads	5.0y	12-Aug-2029	17-Jul-2034																												
A2680	Power supply and distribution to other mine site components	5.0y	12-Aug-2029	17-Jul-2034																												
A2690	Explosives storage facility	5.0y	12-Aug-2029	17-Jul-2034																												
A2700	Ancillary structures	5.0y	12-Aug-2029	17-Jul-2034																												
A2710	Borrow pits and aggregate and concrete batch plant (Plant expansion)	5.0y	12-Aug-2029	17-Jul-2034																												
Off-Site Infrastructure		5.0y	12-Aug-2029	17-Jul-2034																												
A2720	Transmission line	5.0y	12-Aug-2029	17-Jul-2034																												
A2730	Freshwater supply system (FWSS) intake, pump stations and pipeline	5.0y	12-Aug-2029	17-Jul-2034																												
A2740	Airstrip and airstrip access road	5.0y	12-Aug-2029	17-Jul-2034																												




- Critical Remaining Work
- Remaining Work
- summary

TASK filter: Year 6 to 10.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project 6 - Year +11 to Year +18

Activity ID	Activity Name	Original Duration	Start	Finish	2033 2034 2035 2036 2037 2038 2039 2040 2041 2042 2043 2044 2045 2046																																					
					Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q											
Water Treatment																																										
A2960	Neutralization of Low Grade Ore (LGO) Stockpile runoff with lime before discharge along with tailings to TSF C	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A2970	Treatment of waters from the Open Pit and runoff from the Upper and Lower Waste Stockpiles treated by Metals WTP	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A2980	Metals WTP treated water is used at the mill and excess treated water conveyed to WMP	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A2990	Excess TSF C Pond water treatment at Membrane WTP and discharge to the WMP, if req'd due to prevailing climate condition	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
Water Management Structures																																										
A3000	Water Management Pond relocated to accommodate continued filling of TSF C (Year +12)	1.0y	12-Jul-2035	06-Jul-2036		12-Jul-2035																			06-Jul-2036																	
Mine Service and Haul Roads																																										
A3010	In-pit haul roads – Expansion to service pit expansion	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
Components Ongoing Use and Maintenance																																										
A3020	Topsoil stockpiles	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3030	Central and Northern Diversion Systems	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3040	ECD, interception trenches, and pumpback system	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3050	FWR	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3060	Surface drainage for infrastructure	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3070	Mine service roads	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3080	Ex-pit haul roads	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3090	Power supply and distribution	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3100	Explosives storage facility	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3110	Ancillary facilities	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3120	Borrow pits and aggregate sources	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
Off-Site Infrastructure																																										
A3130	Transmission line	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3140	FWSS pumphouse and pipeline	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																
A3150	Airstrip and airstrip access road	8.0y	17-Jul-2034	05-Jun-2042	17-Jul-2034																					05-Jun-2042																

-  Critical Remaining Work
-  Remaining Work
-  summary

TASK filter: Year 11 to 18.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project

7 - Year +19 to Year +23

Activity ID	Activity Name	Original Duration	Start	Finish	2041		2042				2043				2044				2045				2046				2047				2048							
					Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1							
Blackwater Gold Project					5.0y		05-Jun-2042		10-May-2047																													
7 - Year +19 to Year +23					5.0y		05-Jun-2042		10-May-2047																													
Open Pit					5.0y		05-Jun-2042		10-May-2047																													
A3160	Decommissioning of mine fleet and electrical distribution system, de-watering wells, sumps, and related works	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3170	Initiate filling of Pit Lake (See Water Management Structures)	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Processing Plant					5.0y		05-Jun-2042		10-May-2047																													
A3180	Milling of Low Grade Ore (LGO) Stockpile reclaim at 20 Mt per annum (Year +19 to Year +22)3	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Tailings Storage Facility (TSF)					5.0y		05-Jun-2042		10-May-2047																													
A3190	West Dam – Monitoring and maintenance	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3200	Main Dam C – Monitoring and maintenance of dam	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3210	TSF C Pond – Conveyance of supernatant to Open Pit starting Year +19; Serves as process water source;	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3220	TSF C Pond – tailings infill ceases Year +21	3.0y	05-Jun-2042	20-May-2045	05-Jun-2042	[Green bar from 05-Jun-2042 to 20-May-2045]																																
A3230	Main Dam D – Monitoring and maintenance and raised to final elevation of 1,331 masl (Year +20)	1.0y	31-May-2043	25-May-2044		[Green bar from 31-May-2043 to 25-May-2044]																																
A3240	TSF D Pond – Receipt from mine site drainage network; impoundment of PAG, impoundment of tailings starting in Year +21	3.0y	25-May-2044	10-May-2047		[Green bar from 25-May-2044 to 10-May-2047]																																
A3250	TSF D Pond – serves as process water source	3.0y	25-May-2044	10-May-2047		[Green bar from 25-May-2044 to 10-May-2047]																																
A3260	ECD and Pond – Monitoring of dam and pond; Conveyance of captured flows to Open Pit starting Year +19	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Waste Stockpiles (WSF)					5.0y		05-Jun-2042		10-May-2047																													
A3270	Lower Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3280	Upper Waste Stockpile – Resloping, geotechnical stabilization, and monitoring	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Low Grade Ore (LGO) Stockpile					5.0y		05-Jun-2042		10-May-2047																													
A3290	Re-handling of ore to Processing Plant with depletion by Year +23	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3300	Closure and progressive reclamation	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Water Management Structures					5.0y		05-Jun-2042		10-May-2047																													
A3310	Pit Lake – Filling with natural groundwater and TSF C Pond supernatant (Year +20 to Year +23), and ECD Pond	4.0y	31-May-2043	10-May-2047		[Green bar from 31-May-2043 to 10-May-2047]																																
A3320	Lower Waste Stockpile run off directed to TSF C Pond and Upper Waste Stockpile runoff directed to Open Pit	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3330	Continued operation of FWR for mill processing supply and Davidson Creek instream flow needs (IFN)	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
A3340	Continued operation of the Central and Northern Diversion Systems with water conveyed to the WMP and FWR, respectively	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042	[Green bar from 05-Jun-2042 to 10-May-2047]																																
Water Treatment					5.0y		05-Jun-2042		10-May-2047																													




- Critical Remaining Work
- Remaining Work
- summary

TASK filter: Year 19 to 23.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project 7 - Year +19 to Year +23

Activity ID	Activity Name	Original Duration	Start	Finish	Timeline																											
					2041		2042				2043				2044				2045				2046				2047				2048	
					Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	
A3350	Continued operation of the lime neutralization for Low Grade Ore (LGO) Stockpile runoff	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3360	Metals treatment for pit dewatering, the Upper and Lower Waste Stockpiles not required.	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3370	Pit water will be allowed to naturally flow into the Open Pit to aid in pit filling.	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3380	Lower WSP water will be directed to the TSF; Upper WSP water will be directed to the Open Pit and TSF.	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3390	Membrane treatment of excess TSF C water not required as it will be pumped to the Open Pit to aid in pit filling	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
Mine Service and Haul Roads		5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3400	Ex-pit haul roads – Progressive closure and reclamation	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3410	In-pit haul roads – Closure and progressive inundation of in-pit haul roads (Year +19)	1.0y	05-Jun-2042	31-May-2043	05-Jun-2042  31-May-2043																											
Power Supply and Distribution		5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3420	Decommissioning of electrical distribution to Open Pit for drills and shovels	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
Explosives Storage Facility		5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3430	Progressive closure and reclamation	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
Components Ongoing Use and Maintenance		5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3440	Topsoil stockpiles	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3450	Central and Northern Diversion Systems	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3460	ECD, interception trenches, and pumpback system	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3470	FWR Surface drainage for infrastructure	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3480	Mine service roads	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3490	Power supply and distribution	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3500	Ancillary facilities	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3510	Borrow pits and aggregate sources	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
Off-Site Infrastructure		5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3520	Transmission Line	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3530	FWSS pumphouse and pipeline	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											
A3540	Airstrip and airstrip access road	5.0y	05-Jun-2042	10-May-2047	05-Jun-2042  10-May-2047																											

 Critical Remaining Work
 Remaining Work
 summary

TASK filter: Year 19 to 23.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project

8 - Year +24 to Year +45

Activity ID	Activity Name	Original Duration	Start	Finish	2046				2047				2048				2049				2050				2051				2052				2053				2054
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1
Blackwater Gold Project																																					
8 - Year +24 to Year +45																																					
Open Pit																																					
A3550	Filling of Pit Lake to be completed (Year +45)	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Processing Plant																																					
A3560	Decommissioning (Year +24 and Year +25)	2.0y	10-May-2047	29-Apr-2049	10-May-2047																																
A3562	Reclamation (Year +26 onwards)	20.0y	29-Apr-2049	14-Jan-2069					29-Apr-2049																												
Tailings Storage Facility (TSF)																																					
A3570	Reclamation of dams/tailings beaches	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Waste Stockpiles (WSF)																																					
A3580	Lower Waste Stockpile – Rehandling material for reclamation purposes followed by reclamation and monitoring	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
A3590	Upper Waste Stockpile – Reclamation followed by monitoring	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Low Grade Ore (LGO) Stockpile																																					
A3600	Reclaimed with monitoring and maintenance as required	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Topsoil Stockpiles																																					
A3610	Handling and distribution of salvaged soil with eventual closure and reclamation of the stockpiles (Year +26)	1.0y	29-Apr-2049	24-Apr-2050					29-Apr-2049																												
Mine Service and Haul Roads																																					
A3620	Operation and maintenance of roads needed for the Closure phase	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
A3630	Decommissioning and reclamation of other roads	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Power Supply and Distribution																																					
A3640	Operation and maintenance of power supply and distribution needed for the Closure phase	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
A3650	Decommissioning and reclamation of other components of the power supply	22.0y	10-May-2047	14-Jan-2069	10-May-2047																																
Ancillary Structures																																					
A3660	Helipad – Decommissioning and reclamation (Year +25)	1.0y	29-Apr-2049	24-Apr-2050					29-Apr-2049																												
A3670	Camp Facilities – Decommissioning and reclamation (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												
A3680	Construction Laydown Areas – Decommissioning and reclamation (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												
A3690	Truck shop/Mine office – Modification for vehicle servicing, fuel storage and dispensing, for Closure Phases (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												
A3700	Mine site shop, warehousing, offices and accommodations for Closure Phases (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												
A3710	Ready Line and Bulk Fuel Storage area – Decommissioning and reclamation (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												
A3720	Waste Management Facilities – Decommissioning and reclamation (Year +26)	1.0y	24-Apr-2050	19-Apr-2051					24-Apr-2050																												


- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to:	BW	SEB / RT
	Blackwater Decision Statement condition 11.2		

Blackwater Gold Project

8 - Year +24 to Year +45

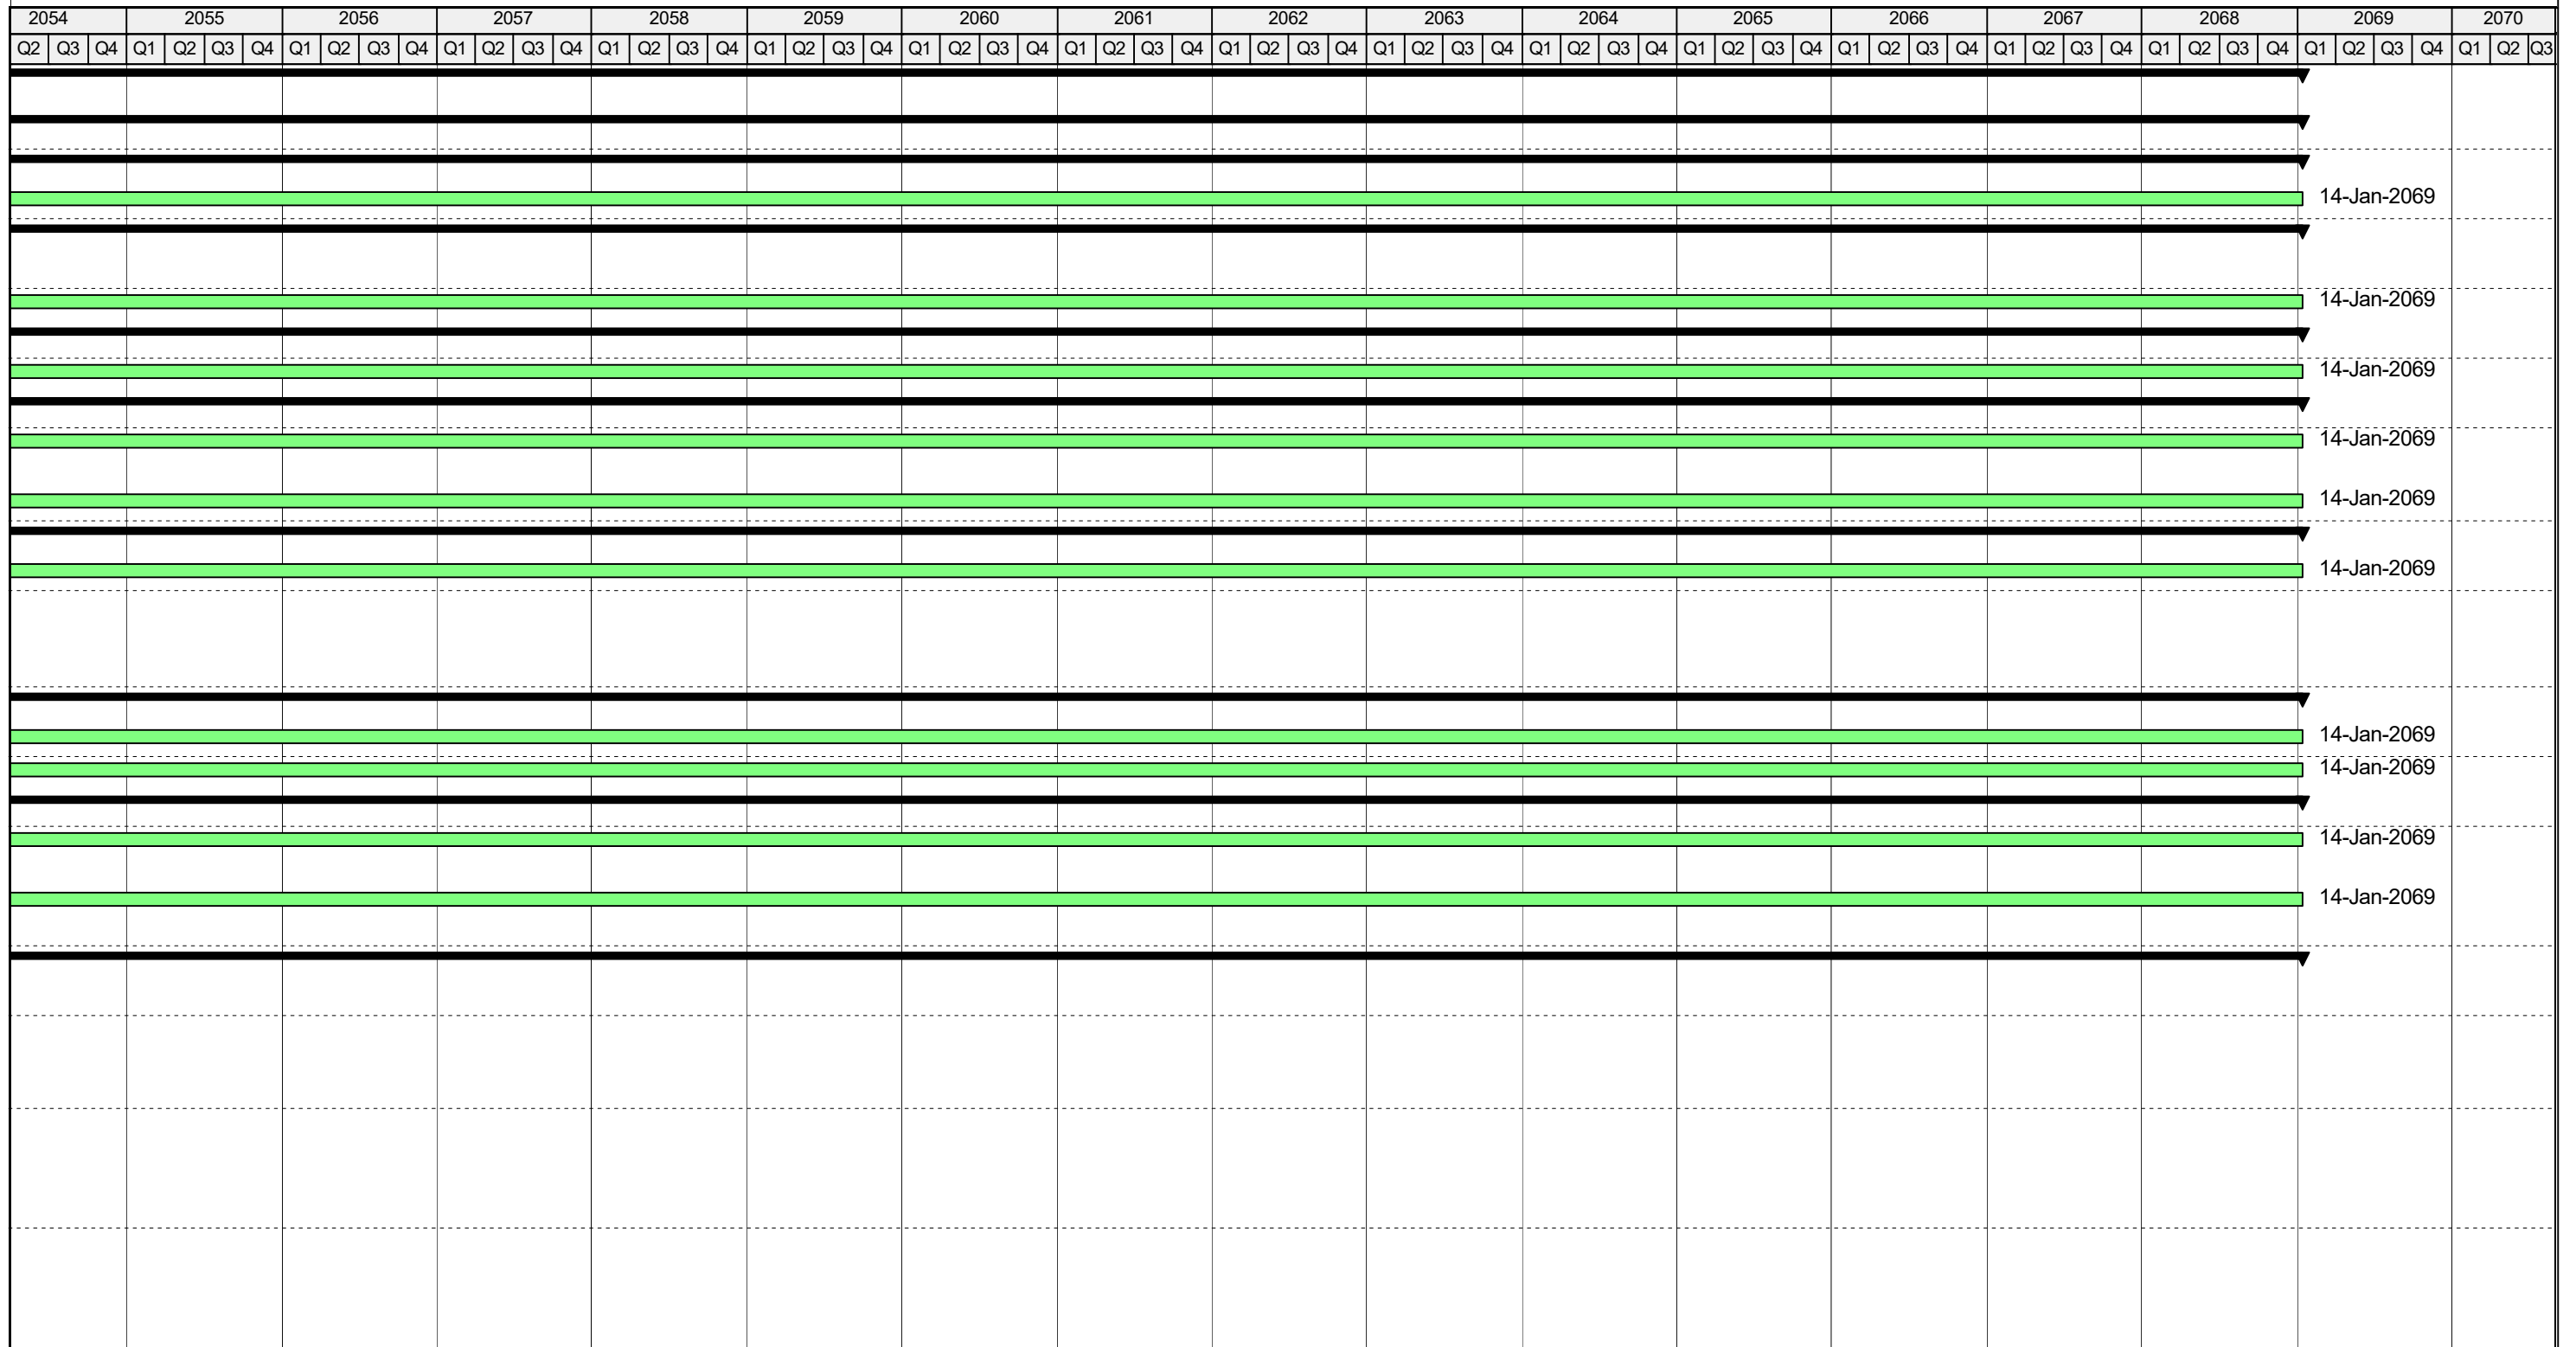

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project 8 - Year +24 to Year +45

Activity ID	Activity Name	Original Duration	Start	Finish	2046				2047				2048				2049				2050				2051				2052				2053				2054				
					Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1				
A3730	Potable and fire water supplies – Decommissioning and reclamation (Year +26)	1.0y	24-Apr-2050	19-Apr-2051													24-Apr-2050																								
A3740	Communications – Decommissioning and reclamation (Year +27)	1.0y	19-Apr-2051	13-Apr-2052																	19-Apr-2051																				
A3750	Security - Replace manned gatehouse with security gate and fencing (Year +27 to Year +44)	17.0y	13-Apr-2052	14-Jan-2069																					13-Apr-2052																
Borrow Pits, Aggregate Screening and Concrete Batch Plants		1.0y	19-Apr-2051	13-Apr-2052																																					
A3760	Decommissioning and reclamation (Year +27)	1.0y	19-Apr-2051	13-Apr-2052																	19-Apr-2051																				
Off-Site Infrastructure		22.0y	10-May-2047	14-Jan-2069																																					
A3770	Airstrip and airstrip access road – Decommissioning and reclamation (Year +25)	1.0y	10-May-2047	04-May-2048					10-May-2047																																
A3780	FWSS pumphouse and pipeline – Decommissioning and reclamation (Year +45)	1.0y	20-Jan-2068	14-Jan-2069																																					
A3790	Transmission Line – Operation and maint for water treatment plants at mine site then decommissioning and reclamation	22.0y	10-May-2047	14-Jan-2069					10-May-2047																																

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project

8 - Year +24 to Year +45

2054			2055				2056				2057				2058				2059				2060				2061				2062				2063				2064				2065				2066				2067				2068				2069				2070		
Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3	Q4	Q1	Q2	Q3												
																																										14-Jan-2069																							
																																										20-Jan-2068																							
																																										14-Jan-2069																							
																																										14-Jan-2069																							

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: WBS .

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT

Blackwater Gold Project 9 - Post Closure Year +46

Activity ID	Activity Name	Original Duration	Start	Finish	2069					2070	
					Q4	Q1	Q2	Q3	Q4	Q1	
Blackwater Gold Project		1.0y	14-Jan-2069	09-Jan-2070							
9 - Post Closure Year +46		1.0y	14-Jan-2069	09-Jan-2070							
Open Pit		1.0y	14-Jan-2069	09-Jan-2070							
A3800	Open Pit pond level maintained at or below design maximum	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
Tailings Storage Facility (TSF)		1.0y	14-Jan-2069	09-Jan-2070							
A3810	Closed when water quality objectives met	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
A3820	Ongoing monitoring and reporting on stability of TSF dams	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
Water Treatment		1.0y	14-Jan-2069	09-Jan-2070							
A3830	Relocation of the Membrane WTP to a new facility adjacent to the ECD	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
A3840	Treated water from ECD, Pit Lake, and TSF C at the Membrane WTP prior to discharge to Davidson Creek	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
Mine Service and Haul Roads		1.0y	14-Jan-2069	09-Jan-2070							
A3850	Operation and maintenance of roads needed for the Post-closure phase	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
A3860	Decommissioning and reclamation of unused roads	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
Power Supply and Distribution		1.0y	14-Jan-2069	09-Jan-2070							
A3870	Operation and maintenance of power supply and distribution needed for the Post-closure phase	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
A3880	Decommissioning and reclamation of other components of the power supply	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070
Security		1.0y	14-Jan-2069	09-Jan-2070							
A3890	Security gate access	1.0y	14-Jan-2069	09-Jan-2070	14-Jan-2069	▶					09-Jan-2070

- Critical Remaining Work
- Remaining Work
- summary

TASK filter: 10 - Post Closure Year 46.

Date	Revision	Checked	Approved
15-Sep-2022	V.2: Prepared pursuant to: Blackwater Decision Statement condition 11.2	BW	SEB / RT
